<u>Titus County Development Projects – Status Update – as of 8 September 2014</u>

Agenda Item 9 - Adult Probation

- Ceiling underway, Floor tile start this week
- Doors scheduled in on the 10th, stain and install with trim
- Millwork started offsite construction of built in desk and cabinets for reception office
- End of September finish

Agenda Item 9 Ratliff Building

- Phase I Elections Administration packages out for bids this week construction start now set for mid/late November: 5-6 weeks of construction
 - 8 separate bid packages totaling an estimated \$56K
- Phase 2 Tax and Vehicle Registration Offices out for bids this week Construction start now estimated mid/late January 2015: 8-10 weeks of construction
 - 8 separate construction packages
 - total estimated at \$130k

Agenda Item 10 - Engineering Fee – Adult Probation

• Additional \$850 needed for Total Engineering Services for engineering fee mandated by state law for mechanical and electrical work over \$8000 (result of vandalism)

Agenda Item 11 - Annex Corner Storefront


- Concept approved by Main Street, final design details needed
- Estimated at \$32k for design, brickwork, energy efficient windows, exterior lighting, doors, awning construction and CM services
- See attached photo and sketches
- Need approval to finish design and put out for bids for construction


Agenda Item 12 – County Computer Room Renovations


- Expansion into existing storage space to provide work areas for computer maintenance and better management of network systems
- Estimated at \$11k Need court approval to go forward for best value bidder
- Detail scope and drawing attached

Agenda Item 13 – Weigh Stations Repair

- To solve rat infestation problem and clean up at two weigh stations on I-30 detailed scope attached
- Estimated at \$7-8k Two proposals offered: \$5500 from Stansell Construction and \$11,200 from DeAngelo Development Recommend the Stansell Construction bid

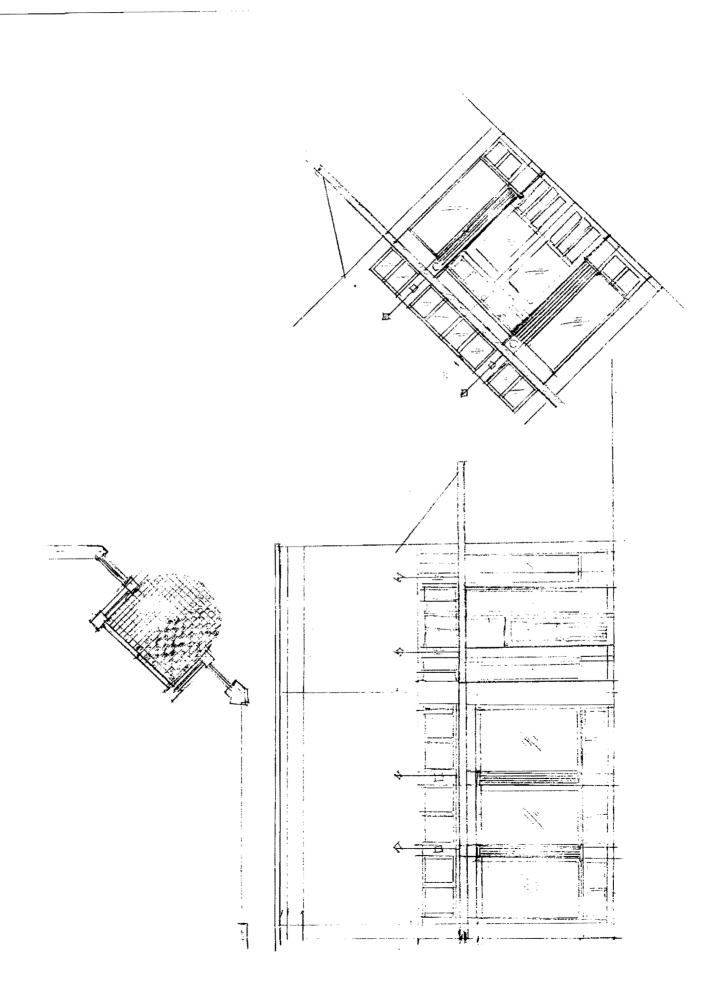

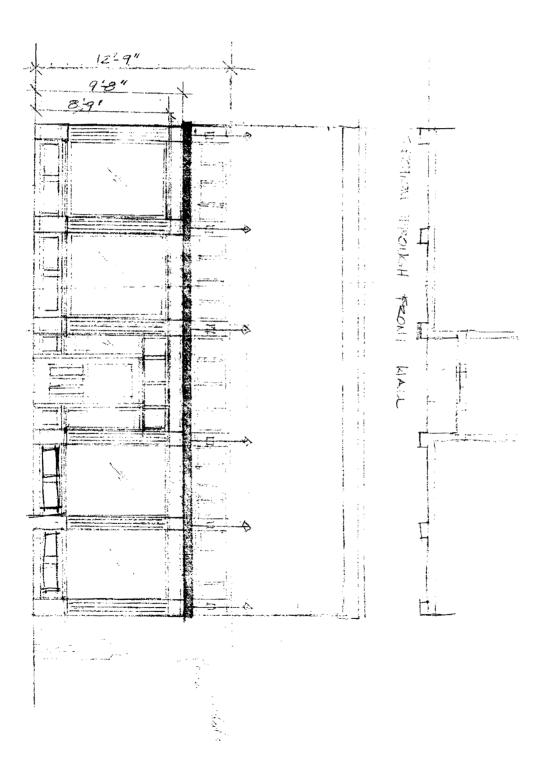



WEST FACADE OF NEW SPACE

